

Project Proposal, Plan and Portfolio Setup

Student Name: Bishal Parajuli

Student ID: SHEA25061

Project Pathway: Startup MVP

Word Count:

Submission Date: 4th July, 2026

GitHub URL:

1. Executive Summary

Although international students in Australia are still experiencing many challenges in gaining graduate employment, there is an ongoing issue of the lack of personalized career support, the unfamiliarity of Australian job application processes and increased competitiveness in the Australian labor force that these students face (Jobs and Skills Australia, 2025; IEAA, 2020; Tran et al., 2023). The proposed Startup MVP will be 'Generative AI Career Readiness Assistant for International students in Australia,' this will integrate resume feedback and interview preparation into one user centric platform using AI. Using Design Science Research (DSR) and Agile Scrum this project includes the use of responsible AI principles, data protection and privacy and ethical governance ensuring the AI used is transparent, fair and trustable as well as providing trusted AI-based decision making (Schwaber and Sutherland, 2020; Hevner, 2007; NIST, 2023). The proposal outlines a practical roadmap for developing and testing the Startup MVP during Project Part B.

1. Executive Summary	2
2. Introduction	3
3. Evidence Review Summary and Gap Analysis	4
4. Problem Statement	5
5. Aim and Objectives.....	5
6. Proposed Solution	6
7. Methodology/ delivery approach.....	8
8. Project Plan	10
8.1 Work Breakdown Structure (WBS)	10
8.2 Gantt Chart	12
8.3 Key Milestones	12
Table 1: Project Milestones	12
8.4 Critical Path	13
Table 2: Critical Path for Proposed Project Plan	13
8.5 Resource needs.....	14
Table 3: Resource Requirements.....	14
9. Risk Management.....	14
9.1 Risk Register	15
Table 4: Summary Risk Register Table.....	15
9.2 RACI matrix	16
Table 5: RACI Matrix for the Proposed Startup MVP	16
10. Ethics, Privacy and Responsible AI.....	17
11. Sustainability and social impact	18
12. Stakeholder and communication plan	18
Table 6: Stakeholder and Communication Plan	18

13. Conclusion and Bridge to Part B	19
14. References	20

2. Introduction

Artificial intelligence (AI) is transforming career development with personalized learning, automated feedback and AI-based decision making (Dwivedi et al., 2023; Kasneci et al., 2023). Despite these advancements, international students in Australia experience difficulty in gaining graduate employment. This difficulty arises from lack of knowledge of Australian employer recruitment processes and high levels of competition as well as because of many barriers that prevent them from having one-to-one access to career counselling (IEAA, 2020; Tran et al., 2023; Jobs and Skills Australia, 2025).

University career services can assist students with career development resources but because the number of students requiring career advice has increased dramatically, they have been unable to assist all students in a timely manner or individually which creates an urgent need for technological solutions (IEAA, 2020). To address these challenges, this project proposes a Startup Minimum Viable Product (MVP), the Generative AI Career Readiness Assistant for International students in Australia. The goal of this product will be to use AI to create resume feedback and help prepare students for interviews tailored to the needs of the Australian labor market using a single platform focused on being user centered (Dwivedi et al., 2023; Kasneci et al., 2023). As part of the design of this project, the goal is to apply responsible AI principles to ensure the career readiness assistant provides personalized and ethical career guidance to international students while ensuring transparency within the decision-making process (NIST, 2023; Department of Industry, Science and Resources, 2019).

With the support of evidence review and gap analysis conducted in assessment 1 and using the feedback from assessment 2, this proposal outlines the project objectives, proposed solution, methodology of implementation, project timeline, method of risk management, ethical considerations, stakeholders engagement and sustainability models. Overall, these sections

ensures to provide a practical and evidence-based roadmap for evaluating and developing the Startup MVP during Project Part B.

3. Evidence Review Summary and Gap Analysis

International students who are studying in Australia still face a number of barriers when it comes to finding graduate-level jobs even though they complete their studies at a high level. Most research has found that these barriers include, but are not limited to, lack of knowledge about how Australian employers recruit employees, lack of professional connections to assist them in finding jobs, unfamiliarity with what Australian employer expect from employees and limited access to personalized career guidance (IEAA, 2020; Jobs and Skills Australia, 2025; Tran et al., 2023). While universities are working to create career development resources for all students, due to the large number of students needing assistance, the ability for each university to be able to provide personalized career development is severely limited.

The new technological advancements made in Generative Artificial Intelligence (GenAI) can become the stepping stone for the intelligent feedback on resume, interview preparation, personalized conversations, career coaching and more (Dwivedi et al., 2023; Kasneci et al., 2023; Michel-Villareal et al., 2023). Various research indicates that GenAI can enhance the learning experience of the students by delivering instant, adaptive, and context-aware feedback while applying for their jobs or choosing a career (Kasneci et al., 2023; Dwivedi et al., 2023; Chan and Hu, 2023). However, most of the AI-based career platforms deal just with an individual function, like resume optimization or interview practice, and do not supply an integrated solution tailored particularly to the employment landscape of Australia for international students (Daryanto et al., 2025; LeFebvre, 2025). Moreover, there are some issues related to algorithmic bias, transparency, privacy and reliability which continues to influence the user's trust and responsible adoption of AI technologies (Westman et al., 2021; Buchanan, 2025; Fu and Weng, 2024).

To further develop the opportunity from the literature review, three complementary gap analysis framework were applied. Firstly, the Jobs-to-be-Done (JTBD) framework evaluated the functional, emotional and social needs of international students at all stages of their career development journey (Christensen et al., 2016). JTBD analysis revealed that students need continuous personalized career advice and support as opposed to unconnected tools that can meet individual task needs. The second framework used, the Value Proposition Canvas (VPC), allowed to evaluate the current needs of international students against the capabilities of current AI-based career solutions (Osterwalder et al., 2014). As it stands, current platforms are capable of providing independent functions such as resume reviews, interview practice, job searching and other forms of career related assistance however have limitations in integrating a

single user-centered system that understands the Australian job environment and therefore cannot provide a tailored experience. Lastly, the NIST AI Risk Management Framework (AI RMF), provided valuable insight on how governance, transparency, fairness and privacy should be embedded in the entire life cycle of the AI solution being developed so that trusted AI is promoted (NIST, 2023).

To sum up, the JTBD, VPC and NIST AI Risk Management framework together identified a significant market, design and governance gap. The JTBD and VPC revealed the unmet user needs and limitations in existing AI platforms, while NIST AI RMF highlighted the lack of responsible AI practices. The current AI platforms exposes limitation in delivering an integrated and responsible AI platform available that combines personal resume feedback and interview coaching for international students seeking employment in Australia (Tran et al., 2023; Kasneci et al., 2023; Dwivedi et al., 2023). Therefore, this gap will form the basis of the proposed Startup MVP which has been designed to provide a single user-centric, ethical and practical solution that can also be scaled.

4. Problem Statement

International students in Australia are still facing serious challenges when it comes to finding job after graduating from Australian universities. A number of these barriers include difficulties in understanding Australian recruitment practices, preparing effective resumes, limited confidence during interviews and accessing personalized career guidance (IEAA, 2020; Tran et al., 2023). University career services can provide many forms of support, however they are experiencing increased demands on resources which restricts them from providing each student with continual personal support. Current AI-powered career development platforms do help students complete various task such as resume reviews or mock interviews. However, there is limitation in existing platform which is lacking to deliver an integrated solution that addresses the overall needs of all international students who have entered the Australian Labor Market (Tran et al., 2023; Daryanto et al., 2025; LeFebvre, 2025).

This project aims to create a Startup MVP that integrates personalized AI-based resume evaluation and interview training into a singular, user-centered application. This is an appropriate time to attempt to solve this problem since recent advancements in Generative AI (GenAI) provides the potential for delivering large scale, fair and affordable career-related solutions that will respond to the increasing demand for personalized employability services being experienced by institutions of higher education in Australia (Kasneci et al., 2023; Dwivedi et al., 2023). Moreover, the implementation of responsible AI principles in the proposed solution ensures transparency, fairness and user trust while supporting ethical AI career guidance (NIST, 2023; Department of Industry, Science and Resources, 2019).

5. Aim and Objectives

The aim of this project is to create an integrated user-centered platform as a Startup Minimum Viable Product (MVP), which will provide international students in Australia with an AI-based resume feedback system and interview preparation. Following are some of the most crucial objectives of this proposal:

Objectives:

- By Week 3 of Part B. Finalize the Startup MVP architecture's design and development, which involves defining the user interface and key system features, as well as the responsible AI requirements for resume feedback and interview coaching.
- By Week 6 of Part B, deliver a working MVP that integrates all core features, achieving at least 90% of test cases across all distinct features.
- By Week 8 of Part B, conduct usability testing with 10 international students with at least 80% participants successfully achieving desired output and collect their feedback on the functionality, usability and perceived usefulness.
- By Part B Week 10, work on the final evaluation of the Startup MVP in relation to the system performance, user satisfaction with an average of 4/5 rating and responsible AI considerations, along with the recommendations for the next development and commercialization.

Thus, these objectives ensure to define the key project milestones and measurable deliverables that will help in successful delivery of the proposed Startup MVP during Project Part B.

6. Proposed Solution

The proposed solution outlines a Startup MVP, the Generative AI Career Readiness Assistant for International Students in Australia. This MVP is presented as a user-focused, web-based AI career platform incorporating two major functionalities; AI-based resume review and AI-aided interview preparation.

Current AI-supported career development platforms are generally limited to focusing on one specific function such as optimizing a resume or practicing interviews, however, they do not provide an overall career development experience for international students entering into the Australian labor force (Tran et al., 2023; Daryanto et al., 2025; LeFebvre, 2025). Therefore, the proposed solution brings together the capabilities from above into a singular platform while ensuring that responsible AI principles are embedded into all aspects of the systems' design to facilitate trustworthiness in decision-making processes through transparency, equity and fairness (Department of Industry, Science and Resources, 2019; NIST, 2023; ISO/IEC, 2023).

The platform will enable users to upload their resume and have it automatically reviewed by artificial intelligence (AI). The system will generate personalized recommendations on how to better format their resume, improve the overall quality of their resume's content, choose the most relevant keywords in order to optimize their resume and align their resume with what employers expect from candidates in Australia (IEAA, 2020; Jobs and Skills Australia, 2025). Additionally, the platform will include coaching module for interviews which would generate interview type questions specific to the user's job interests, analyze the user's response and provide the user with useful constructive criticism so they can develop their communication skills and build their confidence in preparing for interviews (Kasneci et al., 2023; Luckin and Cukurova, 2019). Thus, the resume feedback and interview preparation integration into a single platform supports career readiness for international students by improving resume quality, increasing interview confidence and understanding the Australian recruitment processes (IEAA, 2020; Jobs and Skills Australia, 2025; Tran et al., 2023).

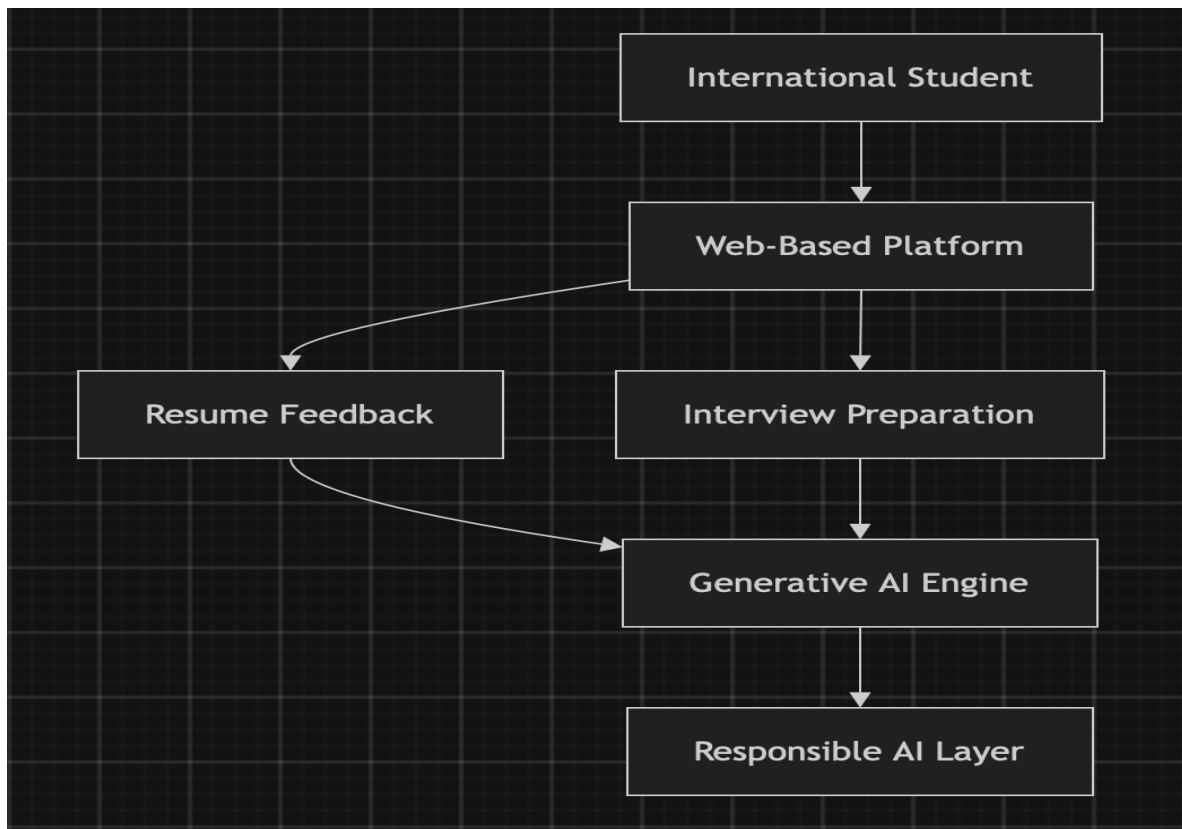


Figure 1: Architecture of the Proposed Startup MVP

The Startup MVP outlined in Figure 1 demonstrates how an AI-enabled career platform can be developed. Students will use this platform where it has two core functional elements, resume feedback and interview preparation. All data entered into the respective elements of the platform is then processed through the central generative AI engine, which will generate

relevant suggestions to assist users achieve their desired objectives with respect to job applications. The platform also includes a responsible AI governance component which uses NIST AI Risk Management Framework to establish principles around responsibility for all decision-making processes supported by AI within the platform (NIST, 2023; ISO/IEC, 2023). The goal of the personalized recommendations generated by AI-enabled career platform is to increase students' levels of employability while also supporting universities existing career support services (Tran et al., 2023; Jobs and Skills Australia, 2025).

As such, the proposed MVP addresses both the evidence review and gap analysis conducted during Assessment 1. Jobs-To-Be-Done (JTBD) identified the requirement for international students to have ongoing and customized career assistance as they transition from education to employment (Christensen et al., 2016). VPC identified the current limitations such as fragmented services of AI-enabled career platforms available today (Osterwalder et al., 2014). The proposed solution aims to develop a single integrated user-centric platform incorporating JTBD requirements while at same time embedding a responsible AI governance model, based on NIST RMF (NIST, 2023).

7. Methodology/ delivery approach

Design Science Research (DSR) will be used as the primary methodology of this project while Agile Scrum will be adopted for delivering the approaches iteratively. DSR is appropriate because the main output of this project will be the design, build and testing of an AI-enabled artefact, the Generative AI Career Readiness Assistant for International Students in Australia. Besides other theory-based research, DSR uses a formalized process for developing new IT artefacts that address real world problems with both systematic design and evaluation (Hevner, 2007; Hevner and Chatterjee, 2010; Peffers et al., 2007).

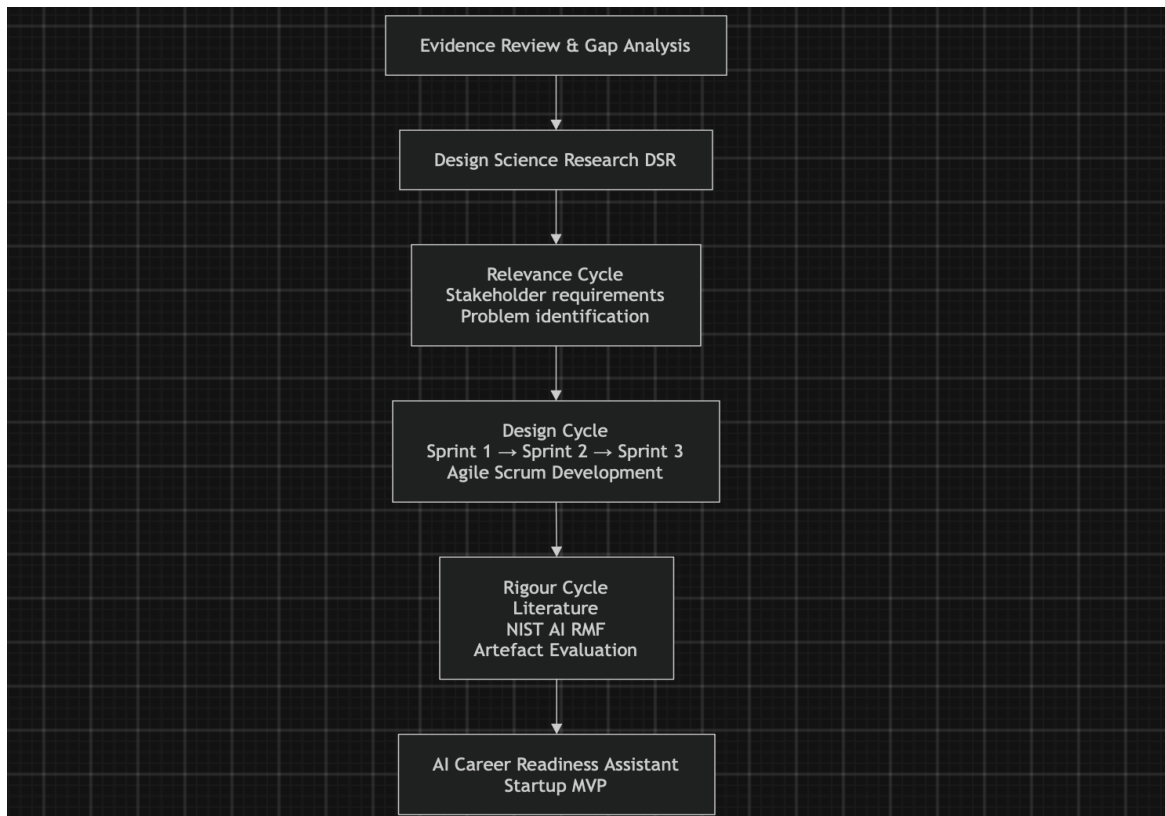


Figure 2: Proposed Methodology and Delivery Approach

Figure 2 illustrates the proposed methodology and delivery approach. It shows how Design Science Research (DSR) guides the overall project while Agile Scrum supports the overall design, development and testing of the proposed Startup MVP. As shown in Figure 2, the project uses Hevner's Three DSR Cycles. The Relevance Cycle is based on the evidence review, stakeholder's needs and gap analysis from assessments 1 and 2. The assessment found that there was a lack of effective integration among current AI Career support services. The Design Cycle provides guidance for the iterative development, testing and improvement of this Startup MVP through Agile Scrum sprints (Hevner et al., 2004). The Rigour Cycle will ensure that the artefact is developed with well-established research and industry frameworks such as Generative AI and NIST AI RMF to ensure transparency and fairness (Dwivedi et al., 2023; NIST, 2023).

The project has adopted an Agile Scrum methodology for the delivery of the project (Schwaber and Sutherland, 2020) to ensure successful implementation. The MVP will be built in three iterative sprints, where each sprint will provide functional enhancements to the product which will then be evaluated against the projects' objectives before proceeding to the next phase. This method of iteration will allow for continued refining of the platform during development and to incorporate the input from both stakeholders and supervisors continuously throughout the development process (Schwaber and Sutherland, 2020).

The preference of DSR over other methodologies is based upon the fact that the main deliverable of this project is a working functional AI prototype and therefore not theory-based outcomes. The preference for DSR over utilizing Agile scrum exclusively is due to the fact that although the iterative software development process of Agile scrum is essential for the project's overall success as it is equally important that there is systematic evaluation of whether or not the artefacts produced addresses the identified employability gap. Therefore, Agile Scrum provides flexibility through its delivery framework to accommodate both incremental MVP building and continuing improvement throughout all phases of the project life cycle.

8. Project Plan

The Project Plan describes the process in which the proposed Startup MVP will be developed, delivered and tested during the course of this 10-week project period. The Design Science Research (DSR) and Agile Scrum methodology will guide development of the project plan. This includes defining the project scope through a Work Breakdown Structure (WBS), creating an implementation schedule through Gantt Chart, identifying the most important project milestones, outlining the critical path to complete each milestone, and detailing all of the necessary resources needed to successfully deliver the proposed solution.

8.1 Work Breakdown Structure (WBS)

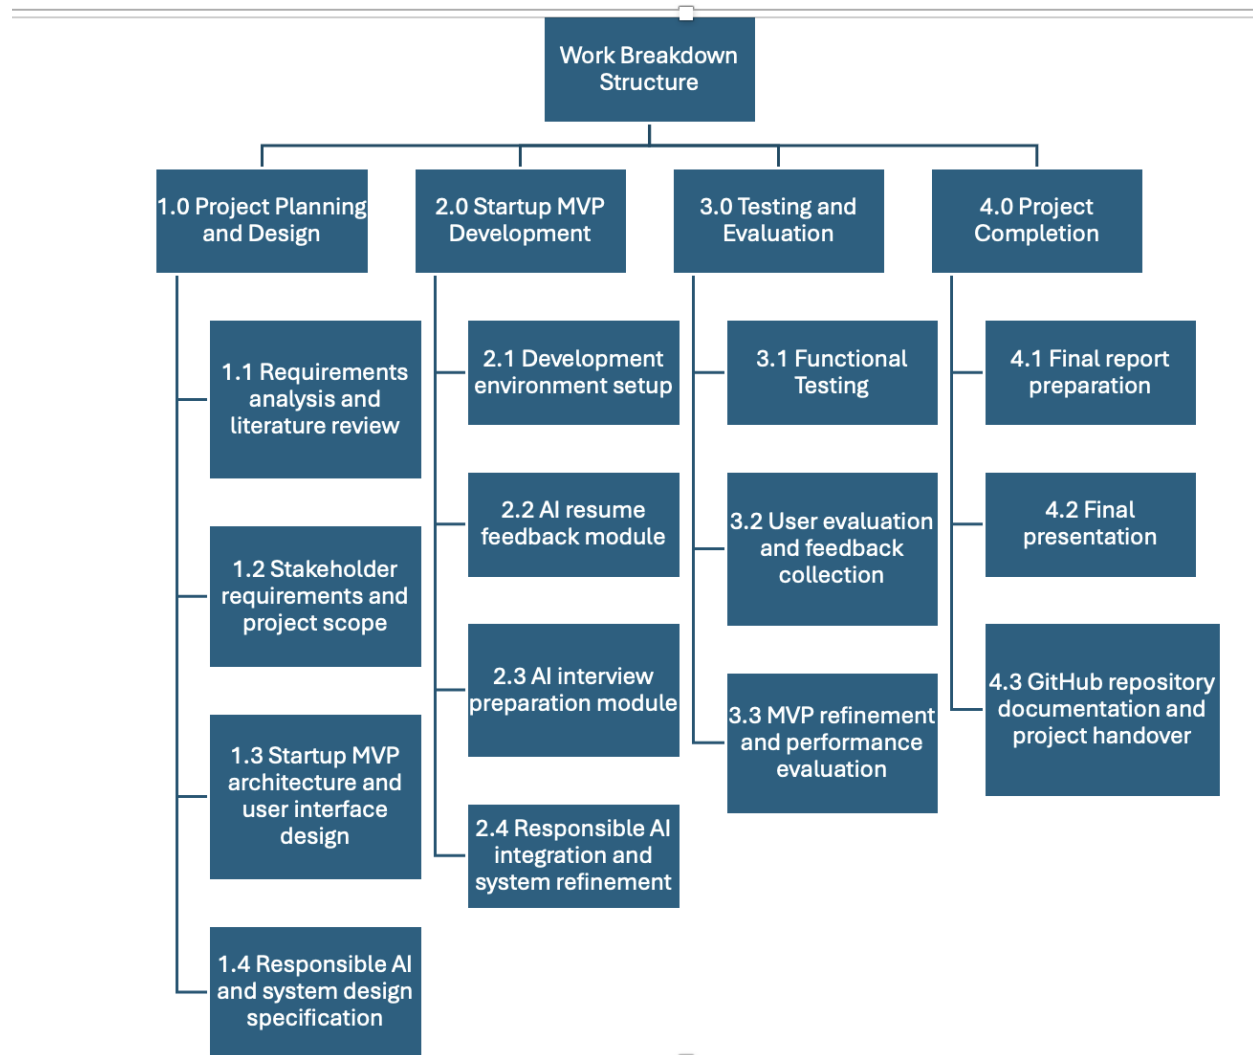


Figure 3: WBS for the proposed Startup MVP

Figure 3 demonstrates the Work Breakdown Structure (WBS) for the proposed Startup MVP, Generative AI Career Readiness Assistant for International Students in Australia. This project has four primary deliverables as listed below:

1. Project Planning and Design
2. Startup MVP Development
3. Testing and Evaluation
4. Project Completion

Each component or deliverable has been further broken down into smaller work packages that provide an outline of the specific tasks needed to complete each deliverable and reach the

overall goals of the project. The WBS will support both scope management and task assignment, in addition to providing a method to monitor the progression of work on the project. The WBS also provides alignment with the Design Science Research methodology and Agile Scrum framework which were selected as the methodologies for this project. Finally, the structured hierarchy presented by the WBS provides a clear roadmap for completing all aspects of the Startup MVP over the proposed ten-week time frame.

8.2 Gantt Chart

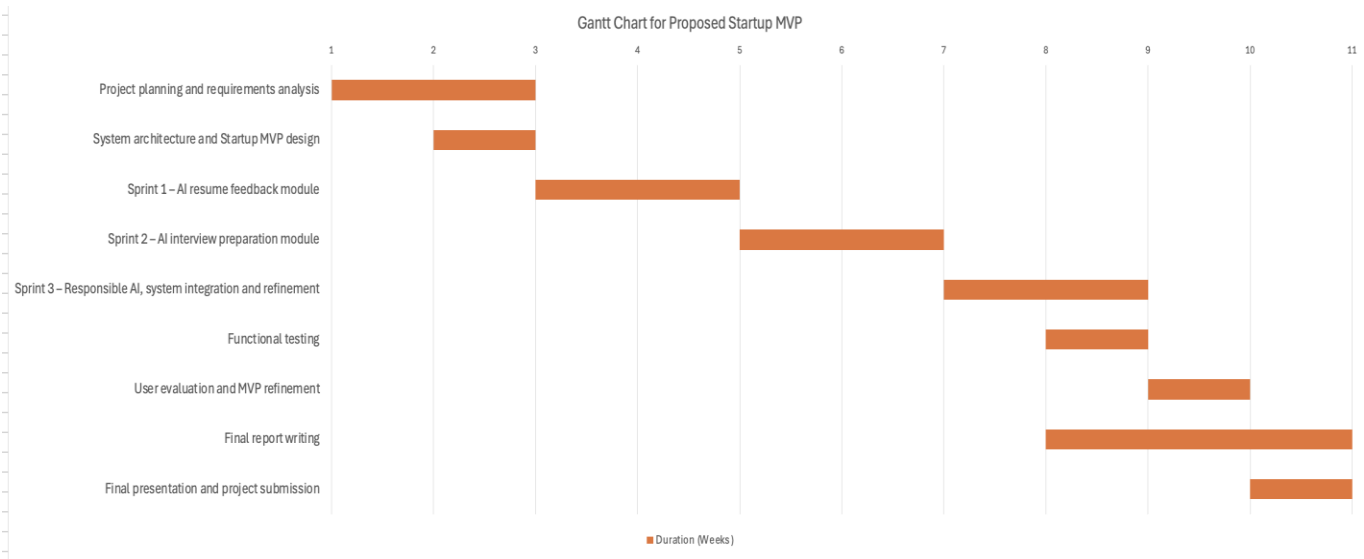


Figure 4: Gantt Chart for the Proposed Startup MVP

The above Figure 4 illustrates the 10 weeks development of the Startup MVP. Project planning, requirements collection and system design will occur first, then the three Agile Scrum Development sprints will be utilized to develop the modules related to AI resume feedback, an interview preparation tool and integrating responsible AI into the product. Once all development has been completed, functional testing and user evaluation will take place. At the conclusion of these activities, the final reports will be developed and presented.

8.3 Key Milestones

The table below shows the key project milestones which will help in monitoring the progress of this project throughout its development phase.

Table 1: Project Milestones

Weeks	Key Milestones
Week 2	Project Requirements analysis and system design completed
Week 4	Sprint 1 (AI resume feedback module) completed

Week 6	Sprint 2 (AI interview preparation module) completed
Week 8	Sprint 3 completed and responsible AI integration finalized
Week 9	Functional testing and user evaluation completed
Week 10	Final report, presentation and project submission completed

Table 1 displays all the key milestones in implementing the proposed Startup MVP from week one through week ten. Each milestone represents completing a large part of an individual project phase with respect to the planning phase, each Agile Scrum development sprint, integration of systems, user testing, user evaluation and final delivery. These milestones serve as a checkpoint for tracking the project's progress and to measure the completion of deliverables, ensuring that the project is successfully delivered within the scheduled plan.

8.4 Critical Path

The table below demonstrates the critical path analysis for the proposed Startup MVP project.

Table 2: Critical Path for Proposed Project Plan

Task ID	Task
A	Project planning and requirements analysis
B	System architecture and Startup MVP design
C	Sprint 1 – AI resume feedback module
D	Sprint 2 – AI interview preparation module
E	Sprint 3 – Responsible AI, system integration and refinement
F	Functional testing
G	User evaluation and MVP refinement
H	Final report writing
I	Final presentation and project submission

The critical path are all the dependent work activities that need to be completed sequentially (A -> B -> C -> D -> E -> F -> H -> I) and represent the shortest possible chain of dependent activities required to deliver a completed project by week 10 as per the plan for completing the Startup MVP. If any of the tasks in this chain do not get done successfully, then the entire last task cannot begin until those have been finished. Activity G, User evaluation and MVP refinement is being done in week 9 however this is happening at the same time as activity H, Final report writing so that any information from users can be incorporated into the project appropriately without impacting the total duration of the project. This simultaneous execution

of these two tasks allows us to make better use of our allotted project time while still meeting our intended delivery date.

8.5 Resource needs

The table below shows the resources that are required to support the development and delivery of the Startup MVP, Generative AI Career Readiness Assistant for International Students in Australia.

Table 3: Resource Requirements

Resource Category	Resource	Purpose
Hardware	Computer/Laptop	Startup MVP development and testing
Software	Python, Visual Studio Code	Application development
Software	GitHub	Code repository
Software	OpenAI API	Generative AI capabilities
Software	Microsoft Word	Documenting and reporting
Research resources	Academic databases	Evidence gathering and literature review
Standards	NIST AI RMF	Responsible AI implementation
Human Resources	Student researcher	Project development and management
Human Resources	Academic supervisor	Project guidance and review
Human Resources	User Participants	Usability testing of delivered platform

The proposed Startup MVP is going to need some combinations of Hardware, Software, Research resources and Human resources in order to assist with both the development of the Startup MVP as well as evaluate it. For developing the Startup MVP, I plan on utilizing Python, Visual Studio Code, GitHub and the OpenAI API for AI-based application. Additionally, I am planning to utilize MS-Word for documenting this overall project. As for supporting the development of this proposed Startup MVP by providing evidence based development and ensuring that the AI is implemented responsibly, I have identified two main tools. These include academic databases and the NIST AI Risk Management Framework (RMF). Lastly, during the evaluation phase, user participant feedback along with an academic supervisor's feedback will also be beneficial in evaluating my proposed Startup MVP project.

To sum up, the project plan helps in assisting the project owner to monitor their project's progress, evaluate the schedule delays on time and identify what resources are needed for the successful completion of the proposed project.

9. Risk Management

In order to minimize uncertainties which may affect the successful development and delivery of the proposed Startup MVP, effective risk management is crucial.

9.1 Risk Register

The creation of a risk register helps to identify the potential risks and evaluate them in terms of a 3-point Likelihood and Impact Scale (Low/Medium/High) each risk has been rated. These ratings are combined into a single Score (Likelihood x Impact) and subsequently used as an indicator for prioritization of mitigation strategies.

Table 4: Summary Risk Register Table

Risk	Score (L*I)	Mitigation	Owner
Disruptions in OpenAI API service or any unexpected API changes	6	Continuously monitor the API updates and keep a backup of alternative API configurations.	Student
Inaccurate AI-generated resume or interview feedback	9	Conduct regular testing, validate the output by comparing existing career resources and ensure human oversight is implemented to monitor the feedback provided by the system.	Student
User Data Privacy breach during usability testing	6	Minimize the collection of user's personal information and comply with Australian Privacy Principles (APPs).	Student
Scope creep due to the addition of AI features	4	Limit the scope of MVP requirements after Sprint 1 and assess all the changes using a guided change management process.	Student
Delays in finding specific users (international students) for usability testing	9	Communicate with the sponsors requesting to provide users, prepare online testing sessions and manage some backup participants for any uncertainties.	Student + Sponsor
Integration issues between AI modules	6	After each sprint, perform integration testing and try to maintain the same version control with the use of GitHub.	Student
Academic workload limiting development time	6	Plan a weekly schedule, prioritize critical tasks to complete within the project's planned schedule and include contingency time within the project plan.	Student

Software bugs	4	Perform iterative testing throughout the each development stage and try to resolve it before final evaluation.	Student
Delayed project schedule due to illness or personal wellbeing	6	Implement buffer time within project and communicate with the academic supervisor as early as possible seeking guidance and help.	Student
Biased AI recommendations affecting International Students	6	Implement responsible AI principles and monitor the output after each process to ensure fairness and transparency.	Student

Table 4 is a Project Risk Register for this project which identifies likely technical, organisational and project management risks in relation to achieving the desired project outcome. Out of all the risk identified, there are two critical risks with a total risk score of 9 which have high probability of occurrence and impacting the overall success of this project. The risks with the total risk score of 6 also require immediate mitigation as they are the next risks that pose threat to this project. Suitable mitigation strategies have therefore been identified for each of these risks and have been formulated to mitigate both the likelihood and the impact of them prior to their occurrence affecting the delivery of the project. The student will be the risk owner of all identified risks as the project is an individual project and appropriate risk monitoring activities will take place at each Agile Scrum Sprint. This proactive approach to managing risk will enable informed decision making by the student, minimize uncertainty associated with the project and improve the chances of delivering a functional and ethically responsible Startup MVP by the scheduled date.

9.2 RACI matrix

The RACI matrix helps to define the roles and responsibilities of key stakeholders who are involved in this project. For this project the RACI matrix table is presented below:

Table 5: RACI Matrix for the Proposed Startup MVP

Activity	Student	Academic Supervisor	User Participant
Project Planning	R/A	C	I
Requirement analysis and gathering	R/A	C	I
Startup MVP development	R/A	I	I
AI model testing	R/A	C	C
User evaluation	R/A	C	C
Risk management	R/A	C	I

Final report and presentation	R	A	I
-------------------------------	---	---	---

The Table 5 presents the RACI matrix for the proposed Startup MVP project, Generative AI Career Readiness Assistant for International Students in Australia. This matrix supports for clearly defining the roles and responsibilities of the key stakeholders who are involved in this project activities by identifying who is Responsible (R), Accountable (A), Consulted (C) and Informed (I). As this project is being developed and designed by the student, they are responsible for completing all the project activities.

Overall, the risks that are identified in this section will be continuously monitored and assessed to ensure that the proposed project is completed on scheduled time, cost and scope. Likewise, the mitigation strategies and RACI matrix provide an outline for the project stakeholders to contribute to successful delivery of the proposed Startup MVP.

10. Ethics, Privacy and Responsible AI

The proposed Startup MVP will be created based on the ACS Code of Ethics, specifically; placing public interest first, being honest, competent and improving the overall quality of life (ACS, 2023). An ethical problem that can arise when developing this product is the potential for generative AI to provide a resume feedback and job interview recommendation from the system that are either biased, inaccurate or misleading. This could negatively impact international students who want to gain employment in Australia (Dwivedi et al., 2023). The system will be designed so that the user considers the output of the system to be suggestions or ideas and they should then use other resources such as career services at their university, employers and their own professional judgment to validate the output.

The collection, storage and handling of user data will be in accordance with the APPs of the Privacy Act 1988 (Cth), as well as data minimization to collect only the required information for generating personalized career advice, whilst providing clear privacy notices and applying adequate security measures to protect users' data (Office of the Australian Information Commissioner, 2024). Furthermore, the project will implement the Essential Eight (a set of eight high-level strategic defensive principles from ASD) and implement secure authentication, regular software updates and access controls to mitigate a number of the most commonly encountered Cyber Security Risks (Australian Signals Directorate, 2023).

A combination of the NIST AI Risk Management Framework (AI RMF 1.0) will guide the project's Responsible AI practices. Risks from the use of AI technologies will be identified, assessed, tracked and controlled throughout the entire Agile Scrum Development Lifecycle (NIST, 2023). The startup will also incorporate the Australian AI Ethics Principles into our approach. These

include fairness, transparency, accountability and human-centered where users are informed that AI generated responses are being used when they receive such feedback and review the output of the system on a regular basis to identify potential biases or inaccuracies (Department of Industry, Science and Resources, 2019). Although the proposed Startup MVP is intended as a decision support tool and not an automatic recruitment process, the Startup MVP will take into consideration all aspects of transparency, risk management and human oversight required within the EU AI Act to ensure that the AI technology is developed in a manner consistent with trustworthy and accountable AI practices (OECD, 2019; European Union, 2024).

11. Sustainability and social impact

The sustainability of the proposed Startup MVP, Generative AI Career Readiness Assistant for International Students in Australia embraces all aspects of environmental, economic and social sustainability throughout the design and delivery of the project. From an environmental perspective, the project is adopting Green IT methods in relations to using cloud-based AI services, as opposed to training large language models from scratch, therefore reducing the amount of computational resource consumption and energy requirements (UNESCO, 2024). The project is also socially sustainable as it provides all students with equal access to personalized career advice to international students in addition to what their respective university's career service can provide (Tran et al., 2023). The project will also be accessible to those users who have disabilities as it follows the Web Content Accessibility Guidelines (WCAG 2.2 LEVEL AA) (W3C, 2023). Finally, the Startup MVP will be economically sustainable as it is low-cost method that complements current service delivery system, increases student employability and allows for long term sustainable operation of institutions with minimal wastage of resources over time (Tran et al., 2023; UNESCO, 2024).

12. Stakeholder and communication plan

The stakeholder and communication plan identifies the key stakeholders for the proposed Startup MVP and establish how to best communicate with them throughout the entire project lifecycle.

Table 6: Stakeholder and Communication Plan

Stakeholder	Interest	Influence	Communication mechanism	Frequency
Academic Supervisor	High	High	Weekly supervision meetings, progress reports, email feedback	Weekly
Student Researcher	High	High	Sprint planning, GitHub monitoring, project documentation	Weekly

(Project Developer)				
International Student Participants	High	Medium	Usability testing, platform evaluation, feedback interviews, online surveys	Weeks 8-9
OpenAI API Provider	Medium	High	API documentation, service status monitoring, release notes	As required
Project Sponsor	High	High	Sprint review meetings, project updates and milestone reviews	Fortnightly

Table 6 presents the Stakeholders and Communication Plan that will be used in the proposed Startup MVP. Stakeholders are prioritized based on their level of interest and how influential they are to support effective ownership, make decisions in a timely manner and ultimately deliver a successful project. Communications processes and timeframes will be adjusted for each stakeholder based upon their job function or position, therefore, there will always be adequate opportunity to provide them with updated information regarding the status of the project, gather from them any necessary input to improve the project, and work collaboratively together using the Agile Scrum methodology.

13. Conclusion and Bridge to Part B

The current plan has an outline to show how the proposed Startup MVP, Generative AI Career Readiness Assistant for International Students in Australia, will be developed as part of the proposed structured roadmap. It is committed to providing a user centric, responsible AI solution that can be delivered based on Design Science Research (DSR) and Agile Scrum practices as well as ensuring privacy and ethical risk are managed appropriately along with identifying stakeholders according to established guidelines for responsible AI (Schwaber and Sutherland, 2020; NIST, 2023).

Part B will start at Week 1 when the initial stages of the project will begin which include the initiation of the project, validating requirements, consulting with the stakeholders and setting up the development environment to provide the base for Sprint 1 and all of the additional development, testing and evaluation activities for the Startup MVP.

14. References

Australian Computer Society (ACS) (2023) *ACS Code of Professional Ethics*. Australian Computer Society. Available at: <https://www.acs.org.au/memberships/professional-ethics-conduct-and-complaints.html>

Australian Signals Directorate (2023) *Essential Eight Maturity Model*. Australian Government. Available at: <https://www.cyber.gov.au/resources-business-and-government/essential-cyber-security/essential-eight>

Buchanan, R. (2025) 'Exploring the role of AI in career access through a social justice lens', *Nordic Journal of Transitions, Careers and Guidance*. Available at: <https://njtcg.org/articles/10.16993/njtcg.77>

Chan, C.K.Y. and Hu, W. (2023) 'Students' voices on generative AI: perceptions, benefits, and challenges in higher education', *International Journal of Educational Technology in Higher Education*, 20, article 43. Available at: <https://doi.org/10.1186/s41239-023-00411-8>

Christensen, C.M., Hall, T., Dillon, K. and Duncan, D.S. (2016) 'Know your customers' "jobs to be done", *Harvard Business Review*, 94(9), pp. 54–62.

Daryanto, T., Ding, X., Wilhelm, L.T. and others (2025) 'Conversate: Supporting reflective learning in interview practice through interactive simulation and dialogic feedback'. Available at: <https://doi.org/10.1145/3701188>

Department of Industry, Science and Resources (2019) *Australia's AI Ethics Principles*. Australian Government. Available at: <https://www.industry.gov.au/publications/australias-ai-ethics-principles>

Dwivedi, Y.K. et al. (2023) "'So what if ChatGPT wrote it?' Multidisciplinary perspectives on opportunities, challenges and implications of generative conversational AI for research, practice and policy', *International Journal of Information Management*, 71, article 102642. Available at: <https://doi.org/10.1016/j.ijinfomgt.2023.102642>

European Union (2024) *Regulation (EU) 2024/1689 laying down harmonised rules on artificial intelligence (Artificial Intelligence Act)*. Official Journal of the European Union. Available at: <https://eur-lex.europa.eu/eli/reg/2024/1689/oj>

Fu, Y. and Weng, Z. (2024) 'Navigating the ethical terrain of AI in education: A systematic review on framing responsible human-centered AI practices', *Computers and Education: Artificial Intelligence*, 7, article 100306. Available at: <https://doi.org/10.1016/j.caeai.2024.100306>

Hevner, A.R., March, S.T., Park, J. and Ram, S. (2004) 'Design science in information systems research', *MIS Quarterly*, 28(1), pp. 75–105. Available at: <https://doi.org/10.2307/25148625>

Hevner, A.R. (2007) 'A three cycle view of design science research', *Scandinavian Journal of Information Systems*, 19(2), pp. 87–92. Available at: <https://aisel.aisnet.org/sjis/vol19/iss2/4/>

Hevner, A.R. and Chatterjee, S. (eds) (2010) *Design Research in Information Systems: Theory and Practice*. New York: Springer. Available at: <https://doi.org/10.1007/978-1-4419-5653-8>

International Education Association of Australia (IEAA) (2020) *International Student Employability: A Guide for Australian Education Providers*. 2nd edn. IEAA. Available at: <https://ieaa.org.au/IEAA/IEAA/research/Publication/2020/international-student-employability-a-guidefor-australian-education-providers.aspx>

ISO/IEC (2023) *ISO/IEC 42001:2023 Information technology — Artificial intelligence — Management system*. International Organization for Standardization. Available at: <https://www.iso.org/standard/81230.html>

Jobs and Skills Australia (2025) *International Students Outcomes and Pathways Study*. Australian Government. Available at: https://www.jobsandskills.gov.au/sites/default/files/2025-09/international_students_pathways_and_outcomes_study_report.pdf

Kasneci, E. et al. (2023) 'ChatGPT for good? On opportunities and challenges of large language models for education', *Learning and Individual Differences*, 103, article 102274. Available at: <https://doi.org/10.1016/j.lindif.2023.102274>

LeFebvre, L. (2025) 'AI résumés: learning to improve self-reflection and résumé development', *Frontiers in Education*. Available at: <https://doi.org/10.3389/feduc.2025.1576196>

Luckin, R. and Cukurova, M. (2019) 'Designing educational technologies in the age of AI', *British Journal of Educational Technology*, 50(6), pp. 2824–2838. Available at: <https://doi.org/10.1111/bjet.12861>

Michel-Villarreal, R., Vilalta-Perdomo, E., Salinas-Navarro, D.E., Thierry-Aguilera, R. and Gerardou, F.S. (2023) 'Challenges and opportunities of generative AI for higher education as explained by ChatGPT', *Education Sciences*, 13(9), article 856. Available at: <https://doi.org/10.3390/educsci13090856>

National Institute of Standards and Technology (NIST) (2023) *Artificial Intelligence Risk Management Framework (AI RMF 1.0)*. NIST AI 100-1. Gaithersburg, MD: NIST. Available at: <https://doi.org/10.6028/NIST.AI.100-1>

OECD (2019) *Recommendation of the Council on Artificial Intelligence*. OECD Legal Instruments. Available at: <https://legalinstruments.oecd.org/en/instruments/OECD-LEGAL-0449>

Office of the Australian Information Commissioner (OAIC) (2024) *Australian Privacy Principles*. Available at: <https://www.oaic.gov.au/privacy/australian-privacy-principles>

Osterwalder, A., Pigneur, Y., Bernarda, G. and Smith, A. (2014). *Value Proposition Design: How to Create Products and Services Customers Want*. Hoboken, NJ: Wiley

Peppers, K., Tuunanen, T., Rothenberger, M.A. and Chatterjee, S. (2007) 'A design science research methodology for information systems research', *Journal of Management Information Systems*, 24(3), pp. 45–77. Available at: <https://doi.org/10.2753/MIS0742-1222240302>

Schwaber, K. and Sutherland, J. (2020) *The Scrum Guide: The Definitive Guide to Scrum: The Rules of the Game*. Available at: <https://scrumguides.org/scrum-guide.html>

Tran, L.T., Tan, G., Bui, H. and Rahimi, M. (2023) 'International graduates on temporary post-graduation visas in Australia: Employment experiences and outcomes', *Population, Space and Place*. Available at: <https://doi.org/10.1002/psp.2602>

UNESCO (2024) *Guidance for Generative AI in Education and Research*. Paris: UNESCO. Available at: <https://unesdoc.unesco.org/ark:/48223/pf0000389227>

W3C (2023) *Web Content Accessibility Guidelines (WCAG) 2.2*. World Wide Web Consortium. Available at: <https://www.w3.org/TR/WCAG22/>

Westman, S., Kauttonen, J., Klemetti, A., Korhonen, N., Mannila, L., Mononen, A., Niittymäki, S. and Paananen, H. (2021) 'Artificial intelligence for career guidance: Current requirements and prospects for the future', *IAFOR Journal of Education*, 9(4), pp. 43–62. Available at: <https://doi.org/10.22492/ije.9.4.03>

Appendix A: Updated Project Charter (Revised)

Project: AI Career Readiness Assistant for International Students in Australia

Student: Bishal Parajuli **Pathway:** Startup MVP **Academic Supervisor/Mentor:** Babak Amiri

A revised version of A1 Charter overseeing feedback from academic supervisor and A2 panel feedback.

Problem Statement: A gap analysis done in this project using Jobs-To-Be-Done (JTBD) and Value Proposition Canvas (VPC) methodologies showed that international students in Australia need on-going and integrated career support. However, the tools currently used by universities and existing AI systems are limited to assisting students with individual tasks such as reviewing resumes or providing mock interviews. Since the demand from international students for assistance in their career has been greater than the capacity of the majority of university career service to meet this need, there is a great deal of opportunity for an easily accessed and always available solution which addresses resume preparation and interview readiness as one continuous process instead of two separate processes.

Value Proposition: A Minimum Viable Product (MVP) based on Generative AI that integrates resume and interview support into a single platform available for international students in Australia to extend the existing university career guidance services, not replace them.

Scope In: AI-generated resume feedback, AI-generated interview preparation, Responsible AI Safeguards

Scope Out: Recruitment and Job Matching, Employment Guarantee, Visa or Migration Support, Automated Resume Writing

Stakeholders: Academic Supervisor, Project Developer, International Students, Project Sponsor, OpenAI API Provider

Success Metrics (SMART)

- The Startup MVP provides personalized resume feedback for 100% of the uploaded resumes and offers at least one interview preparation session for the users by Week 6 of Part B.
- Implementation of responsible AI safeguards such as fairness check, transparency, human oversight and verified throughout all modules by Week 8 of Part B.
- At least 80% of the participants from usability testing reported increased confidence in interview preparation, measured by the surveys conducted on Week 8-9 of Part B.

Top 3 Risks

Risks	Mitigation
Inaccurate or Biased AI-generated outputs	NIST AI RMF implementation, Human oversight.
Scope creep during development	Scope lock to resume feedback and interview preparation after Sprint 1.
Limited participants for usability testing	Early recruitment of university international students, request sponsors for backup participants.

Appendix B: Detailed Gantt Chart

The detailed Gantt chart represents the complete project schedule for the proposed Startup MVP which outlines all the project tasks, their durations (in weeks), predecessors and even the project milestones across the planned 10-week implementation period.

Below is the readable screenshot from Excel for the detailed Gantt Chart.

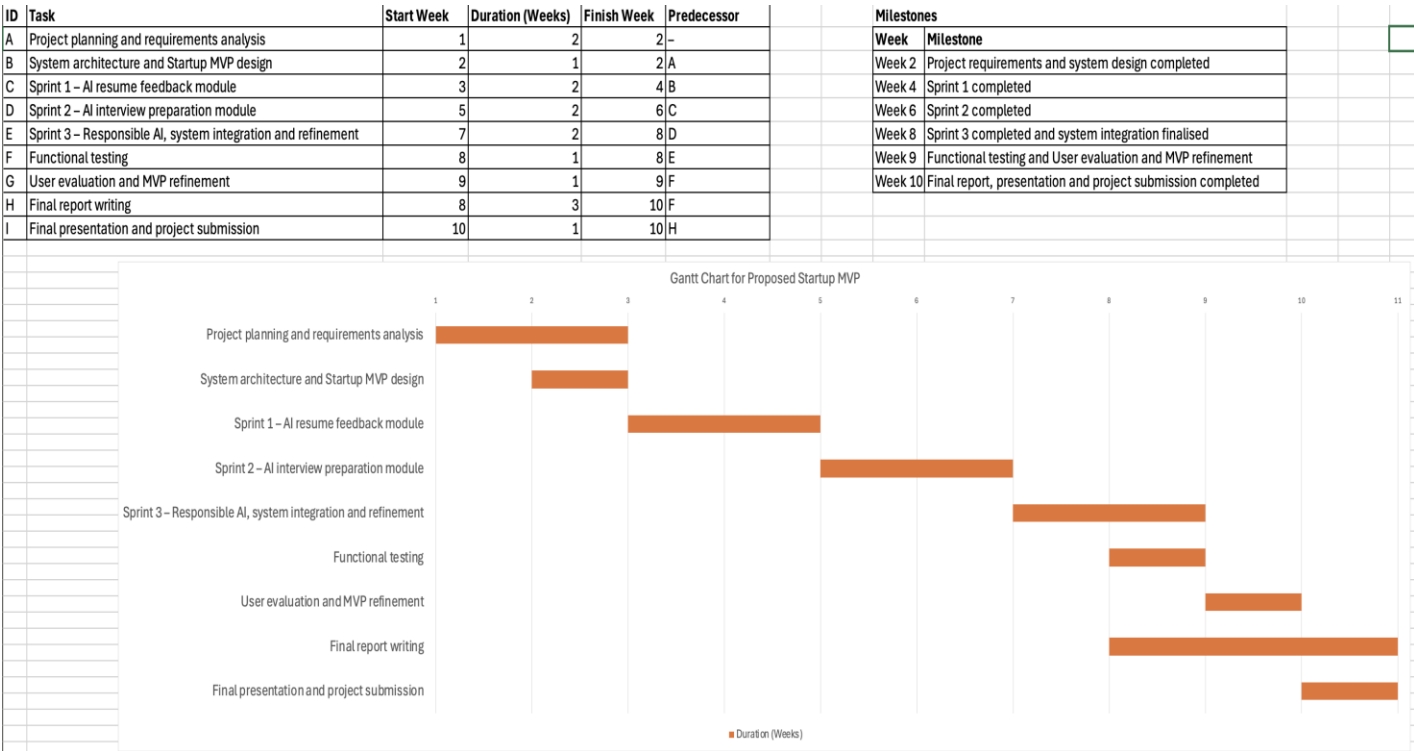


Figure 5: Detailed Gantt Chart for Proposed Startup MVP

Appendix C: Risk Register

Below is the full risk register table which expands the risk management that was presented in Section 10.1 of this report.

Table 1: Full Risk Register Table

Risk ID	Risk	Category	Likelihood (L)	Impact (I)	Score (L*I)	Mitigation	Contingency Plan	Owner
R1	Disruptions in OpenAI API service or any unexpected API changes	Technical	Medium (2)	High (3)	6	Continuously monitor the API updates and keep a backup of alternative API configurations.	Immediately switch to alternative API service and inform the academic supervisor for any further delays.	Student
R2	Inaccurate AI-generated resume or interview feedback	Ethical/Technical	High (3)	High (3)	9	Conduct regular testing, validate the output by comparing existing career resources and ensure human oversight is implemented to monitor the	Flag the affected module and retest it. Make a disclaimer for any identified limitations.	Student

						feedback provided by the system.		
R3	User Data Privacy breach during usability testing	Ethical/Legal	Medium (2)	High (3)	6	Minimize the collection of user's personal information and comply with Australian Privacy Principles (APPs).	Immediately notify the affected participants and academic supervisor for any breach of APPs.	Student
R4	Scope creep due to the addition of AI features	Schedule	Medium (2)	Medium (2)	4	Limit the scope of MVP requirements after Sprint 1 and assess all the changes using a guided change management process.	Keep the additional feature as future improvements and do not work without supervisor sign-off.	Student
R5	Delays in finding specific users (international students) for usability testing	Schedule	High (3)	High (3)	9	Communicate with the sponsors requesting to provide users, prepare online testing	Reduce the sample size with valid justification if required.	Student + Academic Supervisor

						sessions and manage some backup participants for any uncertainties.		
R6	Integration issues between AI modules	Technical	Medium (2)	High (3)	6	After each sprint, perform integration testing and try to maintain the consistent version control with the use of GitHub.	Move to the last stable integration design and isolate the module before merging.	Student
R7	Academic workload limiting development time	Schedule	Medium (2)	High (3)	6	Plan a weekly schedule, prioritize critical tasks to complete within the project's planned schedule and include contingency time within the project plan.	Prioritize WBS tasks and inform academic supervisor if the project seems to be exceeding by more than 1 week.	Student
R8	Software bugs	Technical	Medium (2)	Medium (2)	4	Perform iterative testing	Prioritize the critical bugs, freeze	Student

						throughout each development stage and try to resolve it before final evaluation.	the affected feature until fixed, and re-use the last stable version until resolved.	
R9	Delayed project schedule due to illness or personal wellbeing	Personnel	Medium (2)	High (3)	6	Implement buffer time within project and communicate with the academic supervisor as early as possible seeking guidance and help.	Use additional buffer time if needed, reprioritize the tasks delayed and apply for extension.	Student
R10	Biased AI recommendations affecting international students	Ethical	Medium (2)	High (3)	6	Implement responsible AI principles and monitor the output after each process to ensure fairness and transparency.	Adjust the prompts before enabling the features, avoid the affected recommendations and review the feature for any errors.	Student

Appendix D: RACI matrix

This appendix provides an expanded version of the RACI matrix table from Section 10.2 of this report.

R=Responsible, A=Accountable, C=Consulted, I=Informed

Table 2: Full RACI Matrix Table

Activity	Student (Project Developer)	Academic Supervisor	International Students Participants	OpenAI API Provider	Project Sponsor
Project Planning and Requirement Analysis	R/A	C	I	-	I
Stakeholder requirements and scope definition	R/A	C	I	-	C
Startup MVP architecture and UI design	R/A	C	I	-	I
Responsible AI and System design specification	R/A	C	I	I	I
Sprint1- AI resume feedback module build	R/A	I	I	C	I
Sprint 2- AI interview preparation module build	R/A	I	I	C	I

Sprint 3- Responsible AI integration	R/A	C	I	C	I
Functional Testing	R/A	I	I	I	I
Usability testing protocol design	R/A	C	C	-	C
Usability testing protocol execution	R/A	I	C	-	C
MVP refinement based on feedback	R/A	C	I	I	I
Compliance review on Responsible AI	R	A	I	I	I
Final report and presentation	R	A	I	-	I
GitHub Repository documentation and handover	R/A	I	-	-	I

Appendix E: AI Use Statement

Tools used and purpose

ChatGPT and Claude: To understand the feedback for A1 and A2 provided by the lecturer so that I can incorporate those feedbacks while working on my A3. To check in-text citations against the reference list for Harvard referencing style. To review whether my aim and objectives met the requirements of the SMART criteria. To review the Ethics, Privacy and Responsible AI safeguards explanation against the marking criteria. To confirm if Appendix A (Project Chart) for A3 is genuinely a refined version rather than copy paste and check the WBS and Gantt Chart diagram to confirm they follow consistent ideas throughout the document.

Representative prompts used

1. "Is my refined version of A1 for evidence review summary and gap analysis for A3 presents the same ideas without clashing its originality?"
2. "Check my architecture diagram for my proposed MVP and suggest changes if needed."
3. "Which methodology or delivery approach can strongly support my proposed solution? I am planning to work on hybrid approaches, DSR and Agile Scrum. So, rate my analysis and show the strengths and weakness of these adoptions."
4. "What can be the one ethical dilemma for my proposed solution?"
5. "What were the six elements required for Appendix A and revise that A1 version so that I can be consistent with A3 refined version? Avoid suggesting any new ideas because I just want to understand the feedback from A1 and A2 and work to refine A3 Project Chater.

6. “What additional components should I use to make an expanded version for risk register and RACI matrix to avoid having same tables across different section of the document.”

How I verified outputs

- All the suggested corrections for references or citations were rechecked against my actual reference list.
- The suggested SMART objectives were reviewed against my project’s scope and criteria to ensure they are achievable and not just predicted.
- The similarity rating for Appendix A was verified by comparing the sentences directly against A1 Charter before finalizing the refined version.
- The suggested methodology and their strengths and weaknesses on my project were compared with my evidence review and other academic sources following the same type of projects.

What I did not use AI for: I did not use AI to create any part of the substantial, analytical information in this assignment. I developed my evidence review, my gap analysis, my methodology justification, and my risk assessment through my own efforts with refinement from A1 and A2 comments. I also relied upon myself for writing my reflective essay. The final decision regarding what elements would be included within the scope of my project, how I would conduct my research and all of the materials that I will include as appendices were mine.
